


TRAFFIC CONTROL

- 10 = 2 TYPE 3 BARRICADES/ 1 SIGNED "ROAD CLOSED"
- 20 = 1 TYPE 1 BARRICADE/ SIGNED "ROAD CLOSED AHEAD"
- 40 = 3 TYPE 3 BARRICADES/ 1 SIGNED "ROAD CLOSED"
- 50 = 1 TYPE 1 BARRICADE/ SIGNED "ROAD CONSTRUCTION AHEAD"
- 60 = 1 TYPE 1 BARRICADE/ SIGNED "BIKE TRAIL CLOSED"

- = 7TH AVE WORK/DETOUR WASHINGTON ST TRAFFIC EAST, SEE SPECIAL PROVISIONS
- = 7TH AVE WORK/DELINEATE WASHINGTON ST TRAFFIC WEST, SEE SPECIAL PROVISIONS
- = WORK ZONE
- = SIGN LOCATION

- NOTE: 1. ALL BARRICADES SHALL HAVE FLASHING LIGHTS
2. WASHINGTON ST DETOUR INCLUDES ALL DETOUR SIGNS FOR EASTBOUND DETOUR AND DRUMS TO MOVE WESTBOUND TRAFFIC AROUND WORK IN 7TH AND WASHINGTON INTERSECTION. THIS WILL BE INCIDENTAL TO 7TH AVE, WASHINGTON ST TO NORTH ST TRAFFIC CONTROL ITEM.
3. CONTRACTOR WILL BE REQUIRED TO PROVIDE FLAGGERS, DRUMS, SIGNS, ADVANCE WARNING SIGNS, WHEN PERFORMING UTILITY WORK IN THE INTERSECTION OF BEECH ST AND 7TH AVE. THIS WILL BE INCIDENTAL TO THE 7TH AVE TRAFFIC CONTROL ITEM.

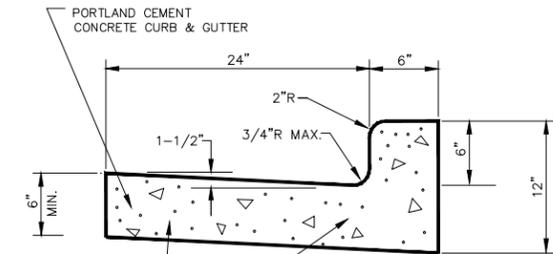

EXPANSION JOINTS TO BE 1/2" THICK AND LOCATED AT 300' INTERVALS, AT ALL INTERSECTIONS WHERE THE TANGENT AND RADIAL CURB AND GUTTER MEET AND 3' ON EACH SIDE OF EVERY INLET OR CATCHBASIN CASTING.

STANDARD CURB & GUTTER SECTION
TYPE D

NOT TO SCALE

NO.	REVISION	DATE	HORIZ SCALE 0 15 30 60	VERT SCALE 0 1.5 3 6
			DESIGNED BY DM	
			DRAWN BY: SPB	
			CHECKED BY DM	
			DATE 2-1-16	
			PROJECT 16-03	
			SHEET 3 OF 13	

VILLAGE OF GRAFTON
BEECH STREET, 7TH AVENUE
9TH AVENUE
 TRAFFIC CONTROL/DETAILS
